MISSION/POSTURE

I JANUARY - 30 JUNE 1967	
MAINTAIN CAPABILITY FOR WORLD-WIDE OPERATION	
FROM PREPARED OVERSEAS BASE	25
MAINTAIN READINESS FOR	
7 DAY QRC FOR SKYLARK	
AND	
15 DAY QRC FOR BLACK SHIELD	
}	
I JULY - 31 DECEMBER 1967	
MAINTAIN CAPABILITY FOR WORLD-WIDE OPERATION	
FROM PREPARED OVERSEAS BASE	25
MAINTAIN READINESS FOR	
7 DAY QRC FOR SKYLARK	
OR	
15 DAY QRC FOR BLACK SHIELD	
ASSUMPTION:	
MISSION REQUIREMENTS CAN BE MET WITH VISUAL	
PHOTO SENSORS ONLY.	25

NRO review(s) completed.

25X1

OXCART PHASE DOWN

ASSUMPTIONS:

AIRCRAFT POSSESSED CY-67

IST HALF

2ND HALF

6 OPNL - A-12 5 OPNL - A-12

2 TEST

I TRAINER (IST QTR)

ITRAINER

240 FLY HOURS 180 FLY HOURS

- STORAGE | PALMDALE
- NO MAJOR MODS/UPDATE -FLIGHT SAFE REQUIREMENTS
- CEASE OPNS (ALL AREAS) 31 DECEMBER 1967
- USE OX ASSETS FOR U-2R/SR-71

AIRCRAFT STANDARD OPERATIONAL READY CONFIGURATION

(SORC)

- INSTALLED EQUIPMENT:
 - INS Α.
 - SC & DM RECORDER
 - ARC-50 COMMUNICATION/RENDEZVOUS SYSTEM
- D. TACAN TO INCLUDE ADDITION OF DF CAPABILITY. (DF CAPABILITY IN ADDITION TO THE PRESENT DME

CAPABILITY IS CONSIDERED A FLIGHT SAFETY ITEM ESSENTIAL FOR AIRCRAFT RENDEZVOUS. ETOR: I JUNE 1967).

E. SSB/HF 25X1 **VOICE RECORDER**

> PROVISIONS FOR ACCEPTING: 2.

25X1

2005/05/16 : CIA-RDP71B00399R000600180004-1

TERMINATED ACTIONS

TYPE II, IV (?)
TYPE V (I JUL)
TYPE VI (I APR)
618 T TUNING MOD
718 T EQUIPMENT CHANGE
HOT FLUX GATE COMPASS
490 T TUNER
D-IO, D-20, IR (OX PORTION)
INSERTION INS

COCKPIT PANEL MOD

330 INS/HSI INTERFACE

MACH TRIM SCHED CHANGE

25X1

FLIGHT SAFE MODS

FACE PLATE HEAT

RELOCATE DICTET RECORDER

SHOCK-PROOF CAMERAS

LOW RPM TACAN & HF

LOW LEVEL FUEL WARN

BOOST PUMP SCHEDULING TANK I.

TANK PUMP CUT-OUT DELETION

DESCENT FLIGHT TEST

210 KNOT DRAG CHUTE

SENSITIVE BALL & RACE

AUTO PILOT IMPROVEMENT

MANAGEMENT

•	A (3 E	N	\mathbb{C}	Υ
				~	

DM & PROJECT OFFICERS

PHASE-DOWN PLAN

MARCH

· COORDINATION

25X1	

· LOGISTICS

NORMAL CHANNELS

AFRDR

25X1

AGENCY

COMMUNICATIONS

POLICY QUESTIONS


* SCOPE COTTON MATERIEL/CONTRACTS

ROUTINE

* SCOPE COTTON CONTRACTS/MATERIEL

SUPPLY

- * SCOPE COTTON
- * SCOPE COTTON
- * SCOPE COTTON



25X

25X

25X

25X

25X

SUPPLY KEY ACTIONS

- * OCTOBER CUT-OFF
- * EQUIPMENT & SPARES LISTINGS
 - · SPARES
 - EQUIPMENT
 - DISPOSITION INSTRUCTIONS
- * ONE TIME REQUIREMENTS
- * SHIPPING, PACKING, STORAGE
- * 5 AIRCRAFT/90 DAY REQUIREMENT

PERSONNEL

ADJUST LEVELS


- * ELIMINATE R&D/TEST SUBSEQUENT JULY
- * MAINTAIN MINIMUM ENGINEERING CAPABILITY
 SUBSEQUENT JULY
- * REDUCE DEPLOYMENT CAPABILITY
- * PROVIDE HEADQUARTERS FOLLOW-ON NAMES


TASKS TO BE TERMINATED

- IRAN
- · CONSTRUCTION
- NEW EQUIPMENT PROCUREMENT

TASKS TO BE CURTAILED

- OVERHAUL & REPAIR
- SPARES PROCUREMENT
- OPERATION & MAINTENANCE

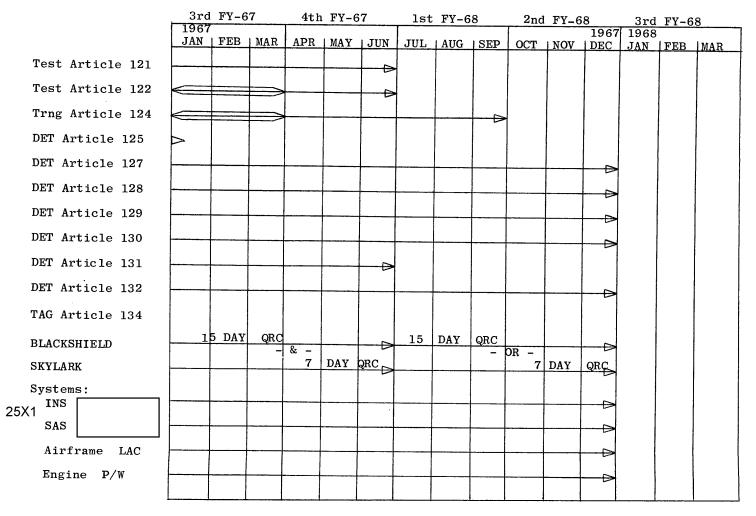

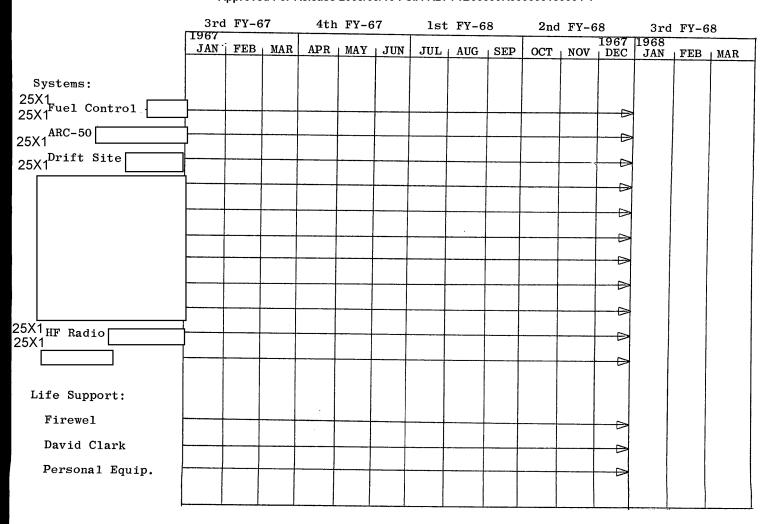

Approved For Release 2005/05/16: CIA-RDP71B00399R000600180004-1

1st FY-68

2nd FY-68

3rd FY-68

4th FY-67

3rd FY-67

1967 1967 | DEC JAN | FEB | MAR APR MAY, JUN JUL, AUG , SEP NOV OCT FEB MAR SUPPORT ACFT: C-130 F 101B 5-8 -F 101F H 43B \Rightarrow UH1F 1 -T-33A 2 -U-3B PERSONNEL: 25) ASSIG. OFFICERS ASSIG. AIRMEN CONTRACT Α В STAFF

Approved For Release 2005/05/16 $\stackrel{\cdot}{\sim}$ CIA-RDP71B00399R000600180004-1

| 3rd | FY-67 | 4th | FY-67 | 1st | FY-68 | 2nd | FY-68 | 3rd | FY-68 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1968 | 1967 | 1967 | 1968 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 | 1967 |

TYPE

I
&
II
OR
IV

TYPE

u & II OR

IV

7

SECURITY

CLASSIFIED CODE NAME:

UNCLASSIFIED NICKNAME: "SCOPE COTTON"

- I. SECURITY OBJECTIVES DURING AND AFTER PHASE OUT.
 - A. PROTECT AGENCY'S ROLE IN OXCART PROGRAM
 - B. COMPLETE NON-AGENCY ATTRIBUTION OF ALL ACTIVITIES

١.	EXISTENCE OF A-12

II. CONTRACTOR CONSIDERATIONS

Ε.

- A. DEBRIEFING OF ALL PROJECT APPROVED PERSONNEL
 - I. O-I AND O-2 BY CO. SECURITY OFFICERS
 - 2. O-3 BY HDQS. SECURITY
 - 3. ITEMS TO BE STRESSED AT TIME OF DEBRIEFINGS
 - A. CONTINUED SECURITY RESPONSIBILITIES
 - B. NO ADMISSION OF PROJECT CONNECTION
 - C. CAN'T CLAIM APPROVAL AS CLEARANCE
 - D. INDIVIDUAL GUIDANCE RE PROBLEM AREAS, E. G., JOB APPLICATION,

PRO V	VIDE	POINT	O F	CONTACT	T WITHIN
CO.	TO F	REFER A	NY	FUTURE	INQUIRIES

RE SECURITY PROBLEMS

- III. DISPOSITION OF CLASSIFIED DOCUMENTS AND HARDWARE
 - A. DETERMINATION WILL BE MADE ON AN INDIVIDUAL BASIS BY TEAM FROM HDQS. VISITING EACH FACILITY.
 - IV. DISPOSITION OF GOVERNMENT FURNISHED EQUIPMENT
 - A. TEAM FROM HDQS. AND PSO WILL DETERMINE ON AN INDIVIDUAL BASIS
 - B. SECURITY GOAL TO ELIMINATE CIA AND/OR PROJECT ATTRIBUTION

- V. FUTURE UTILIZATION OF PROJECT DATA/HARDWARE FOR SALES OR PUBLICITY PURPOSES
 - A. CONTRACTORS SHOULD SUBMIT WRITTEN REQUEST FOR SAME
 - B. THIS WILL APPLY EVEN AFTER OXCART PROGRAM IS PHASED OUT
 - C. POINT OF CONTACT WITHIN OSA WILL BE PROVIDED
- VI. NOTIFICATION OF PHASE OUT TO CONTRACTOR PERSONNEL
 - A. THOSE WHO NEED TO KNOW CAN BE TOLD
 - B. STILL HAVE TO MAINTAIN OPERATIONAL CAPABILITY UNTIL 31 DECEMBER 1967
 - C. HOLD DOWN REQUESTS FOR PROJECT APPROVALS
 AS MUCH AS POSSIBLE

DEFINITIONS

AGE: Aerospace Ground Equipment

COMMON/STANDARD AGE: Item of inventory type, development has been completed; has application to more than one weapon system or equipment.

<u>PECULIAR/DEVELOPMENT AGE</u>: A new item either in the process of being introduced into the inventory as a result of design to support a specific weapon or component.

(NOTE: Above definitions can also be applied to components, spares or hardware.)

INACTIVATION: The procedure required to place an active installation or facility in an inactive or caretaker status, with provisions for reactivation 60 days prior to the beneficial occupancy date, except as otherwise may be specifically directed.

 $\overline{\text{1PE}}$: Industrial Plant Equipment; those items of plant $\overline{\text{equipment}}$ used for cutting, abrading, grinding, shaping, forming, joining, measuring, testing, heating or treating materials or work in process.

GOVERNMENT-FURNISHED PROPERTY: Property in the possession of or acquired directly by the Government and subsequently delivered or otherwise made available to the contractor.

CONTRACTOR-ACQUIRED PROPERTY: Property procured or otherwise provided by the contractor for the performance of a contract, title to which is vested in the Government.

MATERIAL: Property which may be incorporated into or attached to an end item to be delivered under a contract or which may be consumed or expended in the performance of a contract. It includes, but is not limited to, raw and processed material, parts, components, assemblies, and small tools and supplies which may be consumed in normal use in the performance of the contract.

SPECIAL TOOLING: All jigs, dies, fixtures, molds, patterns, special taps, special gauges, other special equipment and manufacturing aids, and replacements thereof, acquired or manufactured by the contractor for use in the performance of contract, which are of such a specialized nature that, without substantial modification or alteration, their use is limited to the performance of such services as are peculiar to the needs of the Government.

SPECIAL TEST EQUIPMENT: Electrical, electronic, hydraulic, pneumatic, mechanical or other items or assemblies of equipment which are of such a specialized nature that, without modification or alteration the use of such items or assemblies is limited to testing in the development or production of particular supplies or parts in the performance of particular services.

FACILITIES: Property, other than material, special tooling, and special test equipment, used for the performance of a contract or sub-contract, including real property and rights therein, buildings, structures, improvements and plant equipment.

SALVAGE: Property recoverable for further use or which because of its worn, damaged, deteriorated or incomplete conditions, or specialized nature, has no reasonable prospect of sale or use as serviceable property without major repairs or alterations but which has some value in excess of its scrap value.

SCRAP: Property that has no reasonable prospect of being sold except for the recovery value of its basic material content.
